


TO-BE Construction Process 7.13.16

45 days allowed by Statute

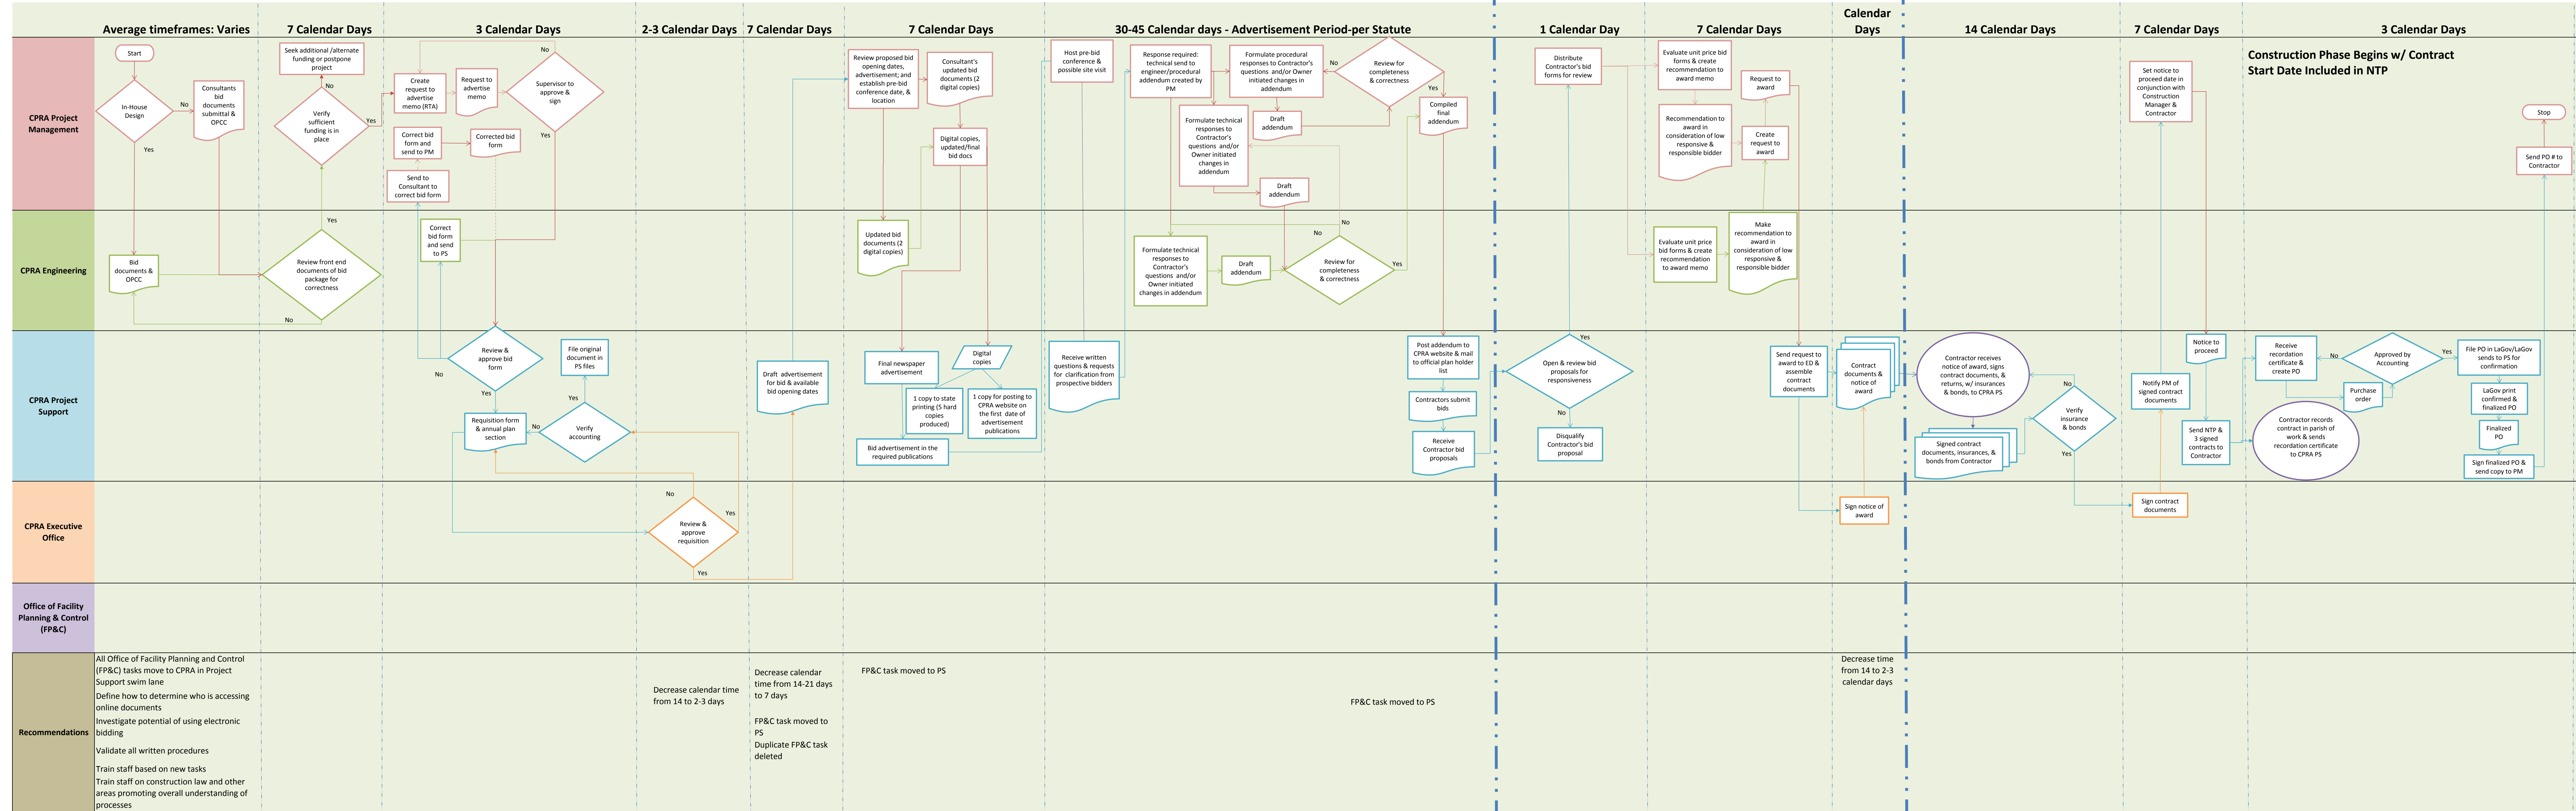

OPCC
RTA
FP&C
PS
PM

Opinion of probable construction cost
Request to advertise
Office of Facility Planning and Control
Project Support
Project Manager

Decrease calendar time from 14 to 2-3 days
Decrease calendar time from 14-21 days to 7 days
FP&C task moved to PS
FP&C task moved to PS
Duplicate FP&C task deleted

FP&C task moved to PS

Decrease time from 14 to 2-3 calendar days
